


**January 27, 2020  
Saugus Middle High School  
School Building Committee Meeting**



KEY MILESTONES
Steel Erection Completed Early May 2019
Floor Slabs Completed June 2019
Building Enclosed September 2019
Brick Completed in October 2019
Windows Completed November 2019
Metal Panels to be Completed in March 2020
Interior Finishes Everywhere in Progress, to be Completed End of February 2020
Auditorium Ceilings Wrapping up
Kitchen EQ Being Installed
Gym EQ Being Installed
Substantial Completion April 17, 2020

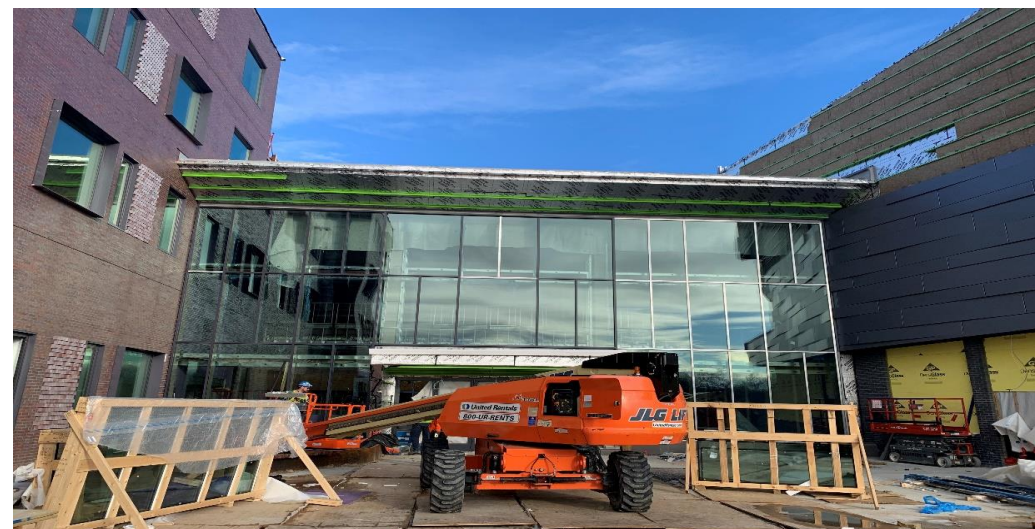

MANPOWER	
Average Daily Site Workforce	169

DIVERSITY STATUS		
Category	Goal	Current
Minority Workforce	15%	18.9%
Women Workforce	7%	2.80%
MBE / WBE Status	10%	7.3%

LEED POINT SUMMARY (LEED GOAL SILVER 58 POINTS)				
	Yes	No	Maybe	Total Available
Design/Owner	46	15	27	88
Construction	13	2	7	22
<b>Total</b>	<b>59</b>	<b>17</b>	<b>34</b>	<b>110</b>
