

# Town of Saugus


## SSO Program Status Update


### Board of Selectmen

August 27, 2013



# Sequence of Construction for the Saugus Sewer System Rehabilitation Program (as of August 2013)

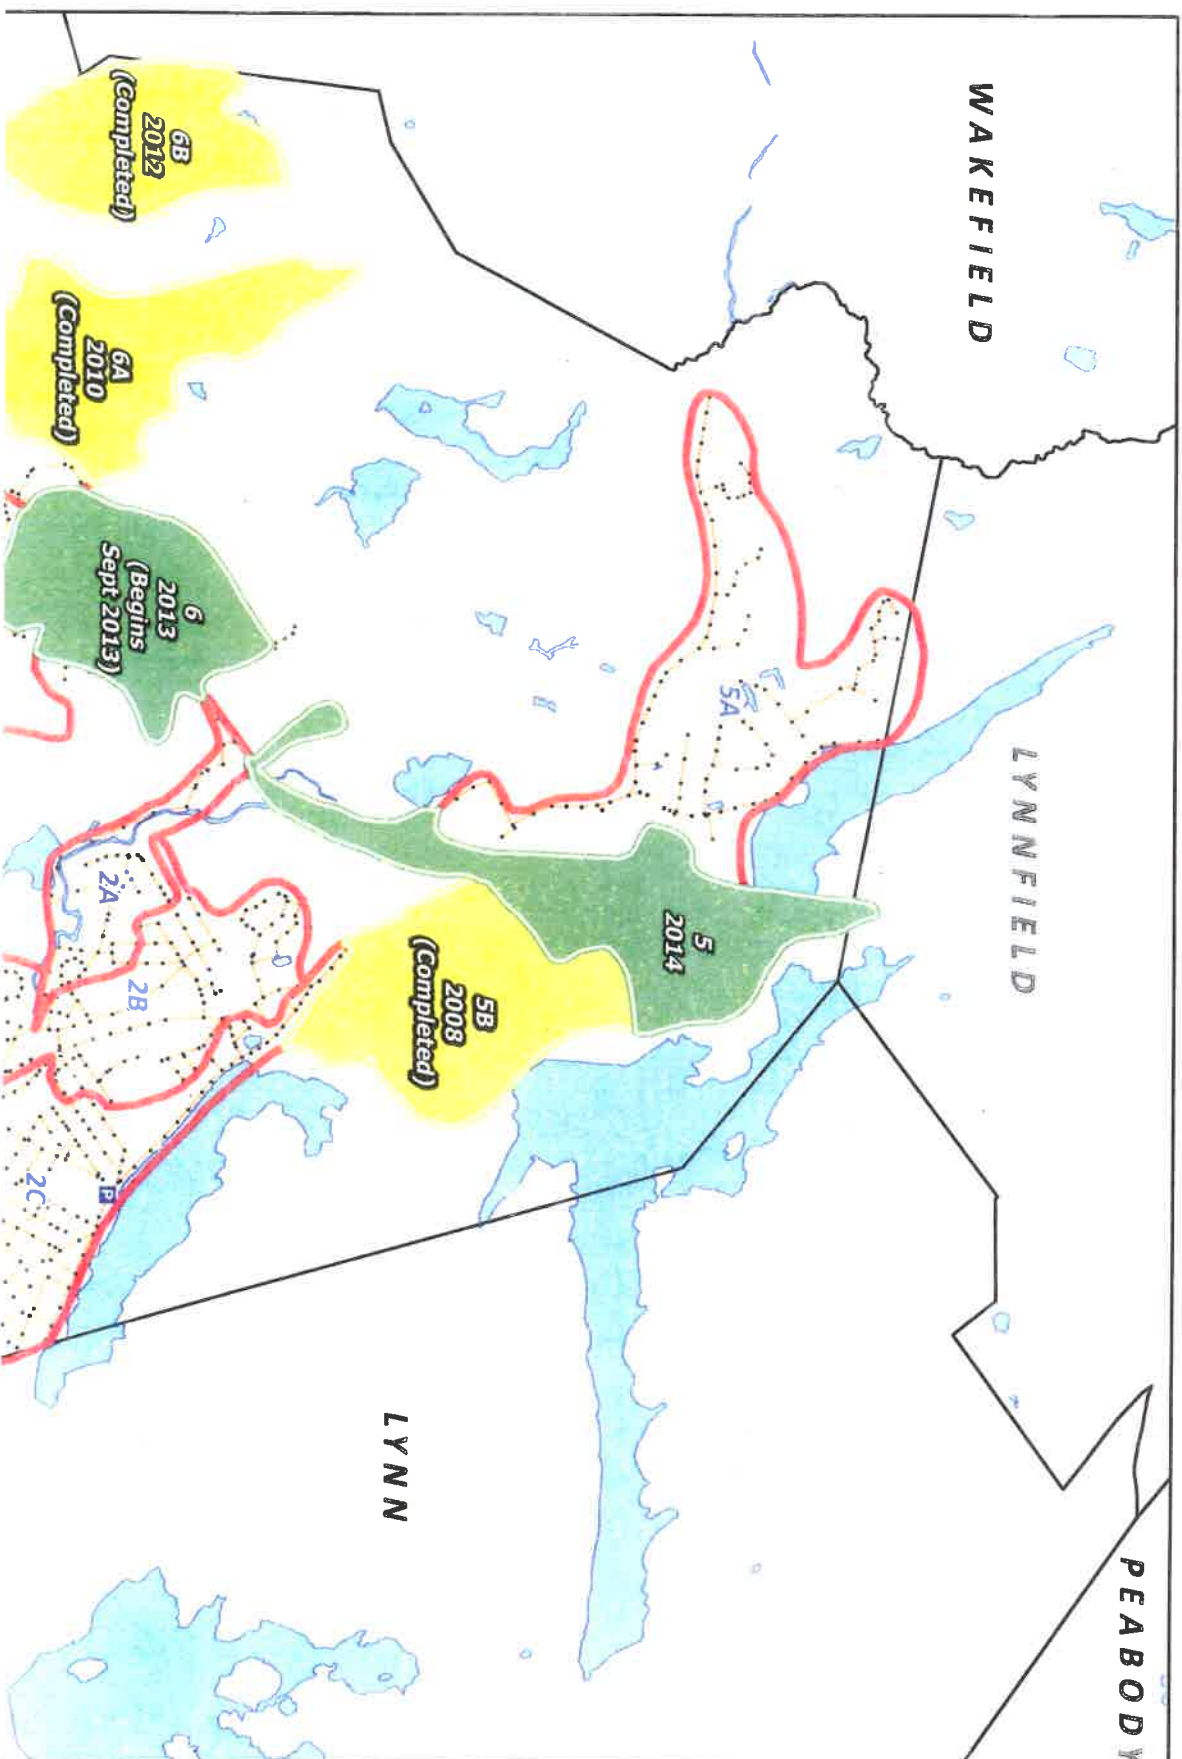

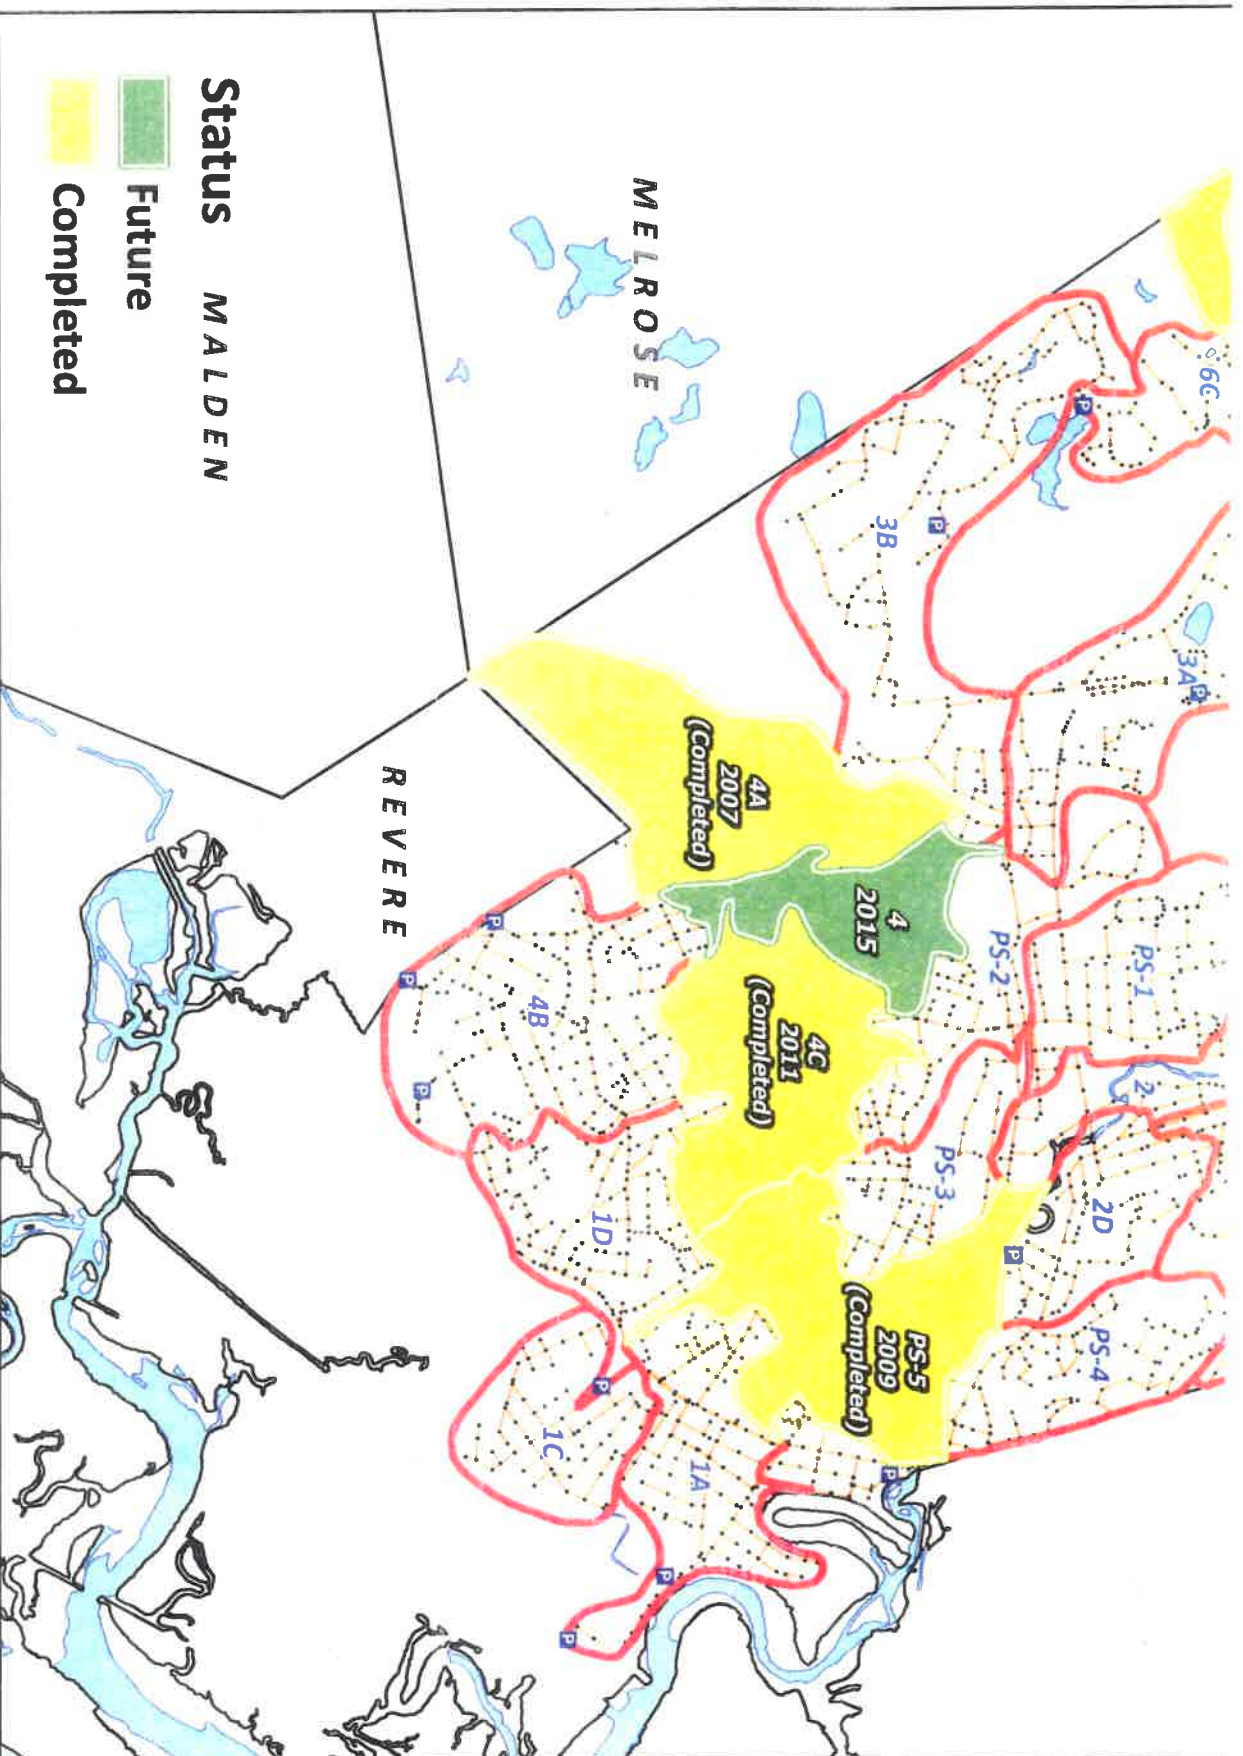


# SSO Program Current Construction Project Status

(as of 8/26/2013)

| Contract Number | Contract Name                       | Status       |
|-----------------|-------------------------------------|--------------|
| 21-12           | 6B Sewer Rehabilitation             | 95% Complete |
| 11-13           | 6 Cured-in-Place Pipe Lining        | Bid Phase*   |
| 12-13           | 6 Service Lateral Connection Lining | Bid Phase*   |
| 13-13           | 6 Manhole Rehabilitation            | Bid Phase*   |
|                 |                                     |              |

\* Bids opened 8/15/13


**Goal to Meet ACO-11,000,000**

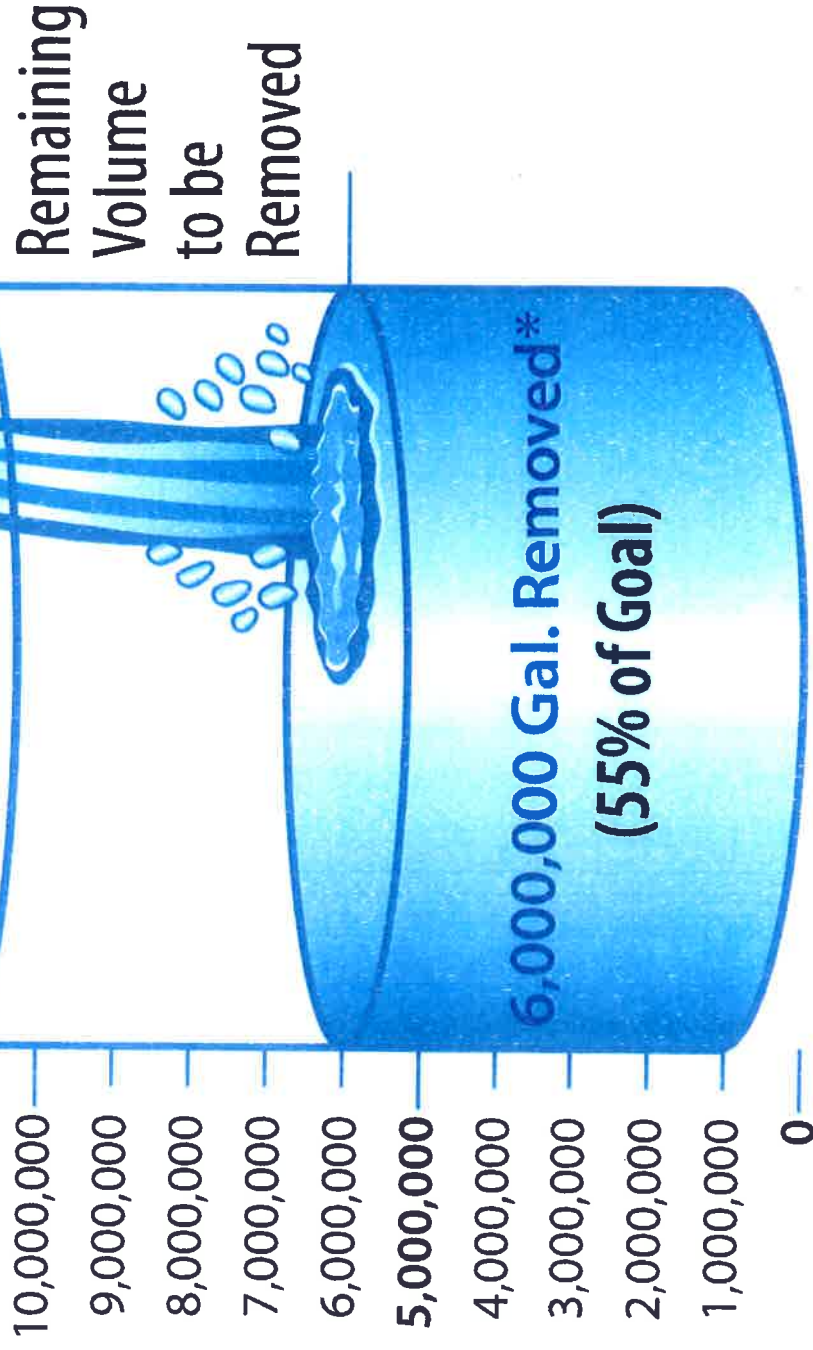


\*Based on a 10-Year Storm Frequency

**Status of I/I Removed as of August 2013**

**Town of Saugus SSO Reduction Program  
Estimated Planning vs. Actual Program Costs**

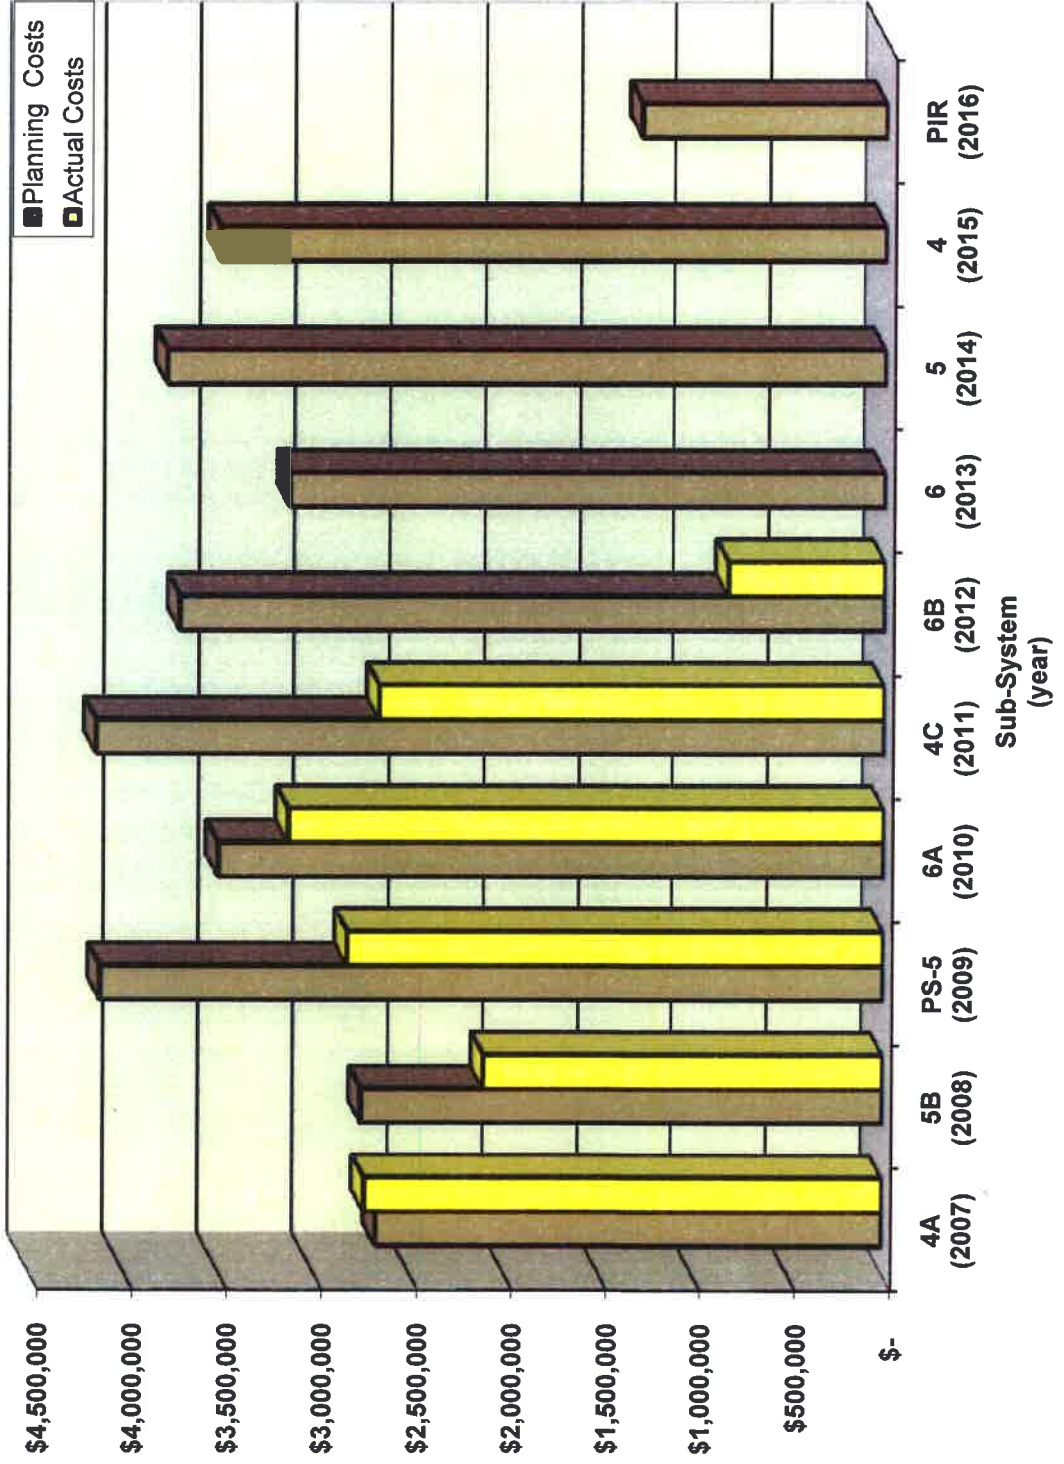

SSO Program Actual vs. Estimated Planning Cost

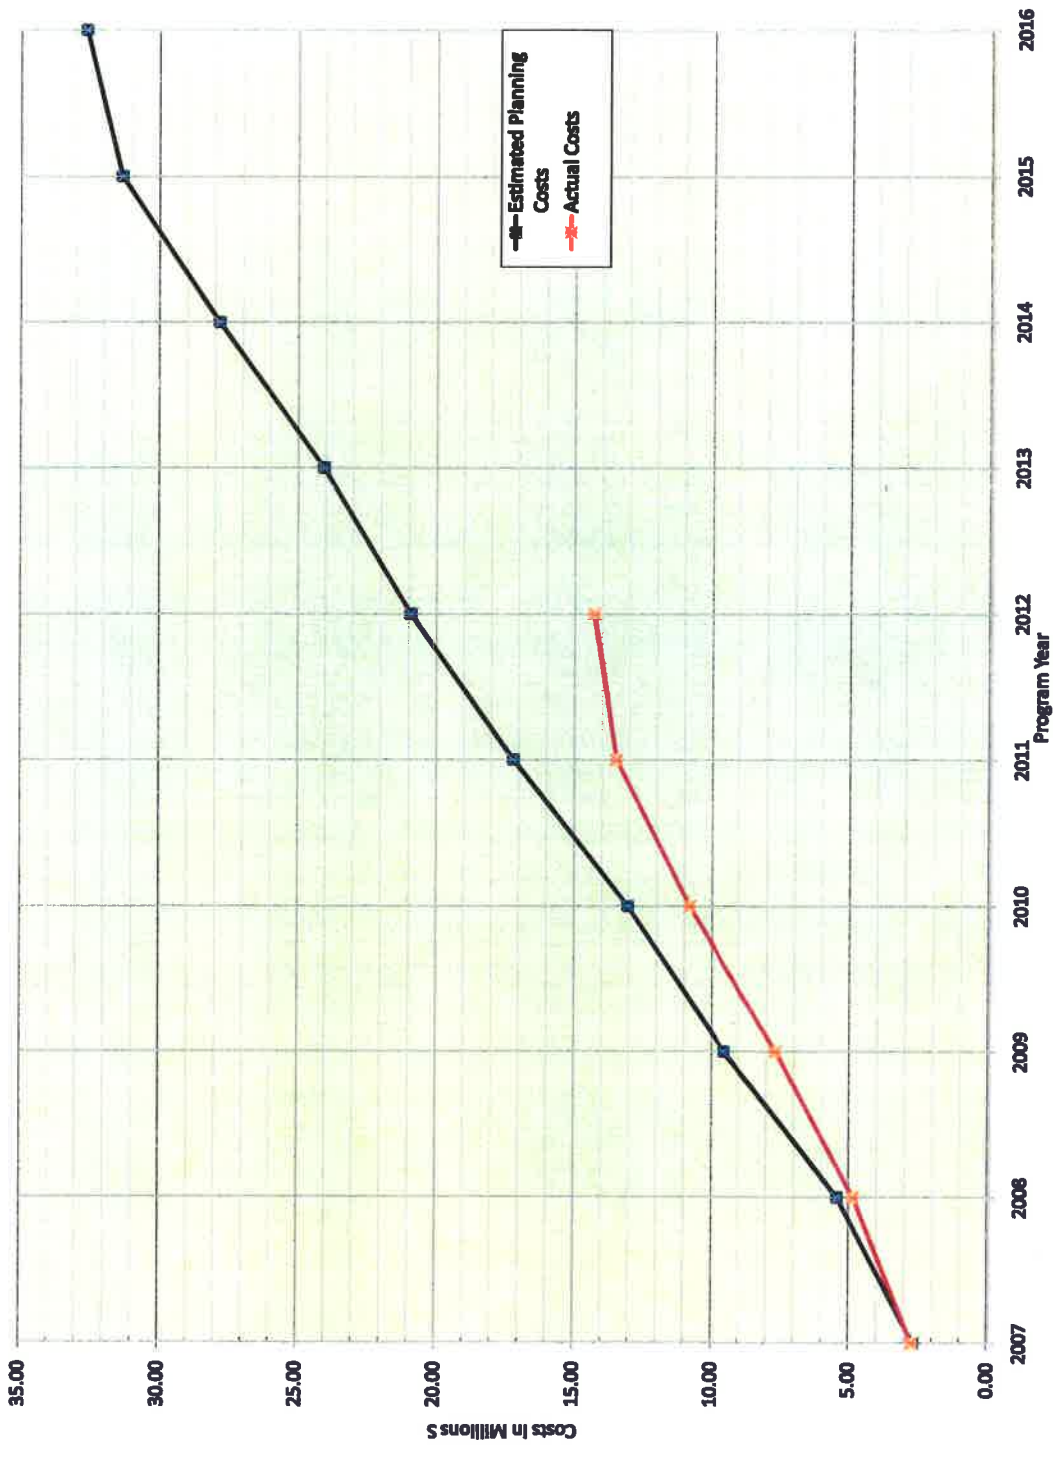

# Private Inflow Program Status

(as of August 2013/ Not incl. 6B)

| Private Inflow Source            | Identified | Removed to Date | % Compliance |
|----------------------------------|------------|-----------------|--------------|
| Sump Pumps Connected to Sewer    | 53         | 49              | 92%          |
| Sump Pumps w/ Flexible Discharge | 263        | 243             | 92%          |
| Floor/Foundation Drain to Sewer  | 3          | 2               | 67%          |
| Stairwall Drain to Sewer         | 1          | 0               | 0%           |
| <b>Total</b>                     | <b>320</b> | <b>294</b>      | <b>92%</b>   |
